JALC PROJECT TIMELINES

Tuesday, January 9, 2024
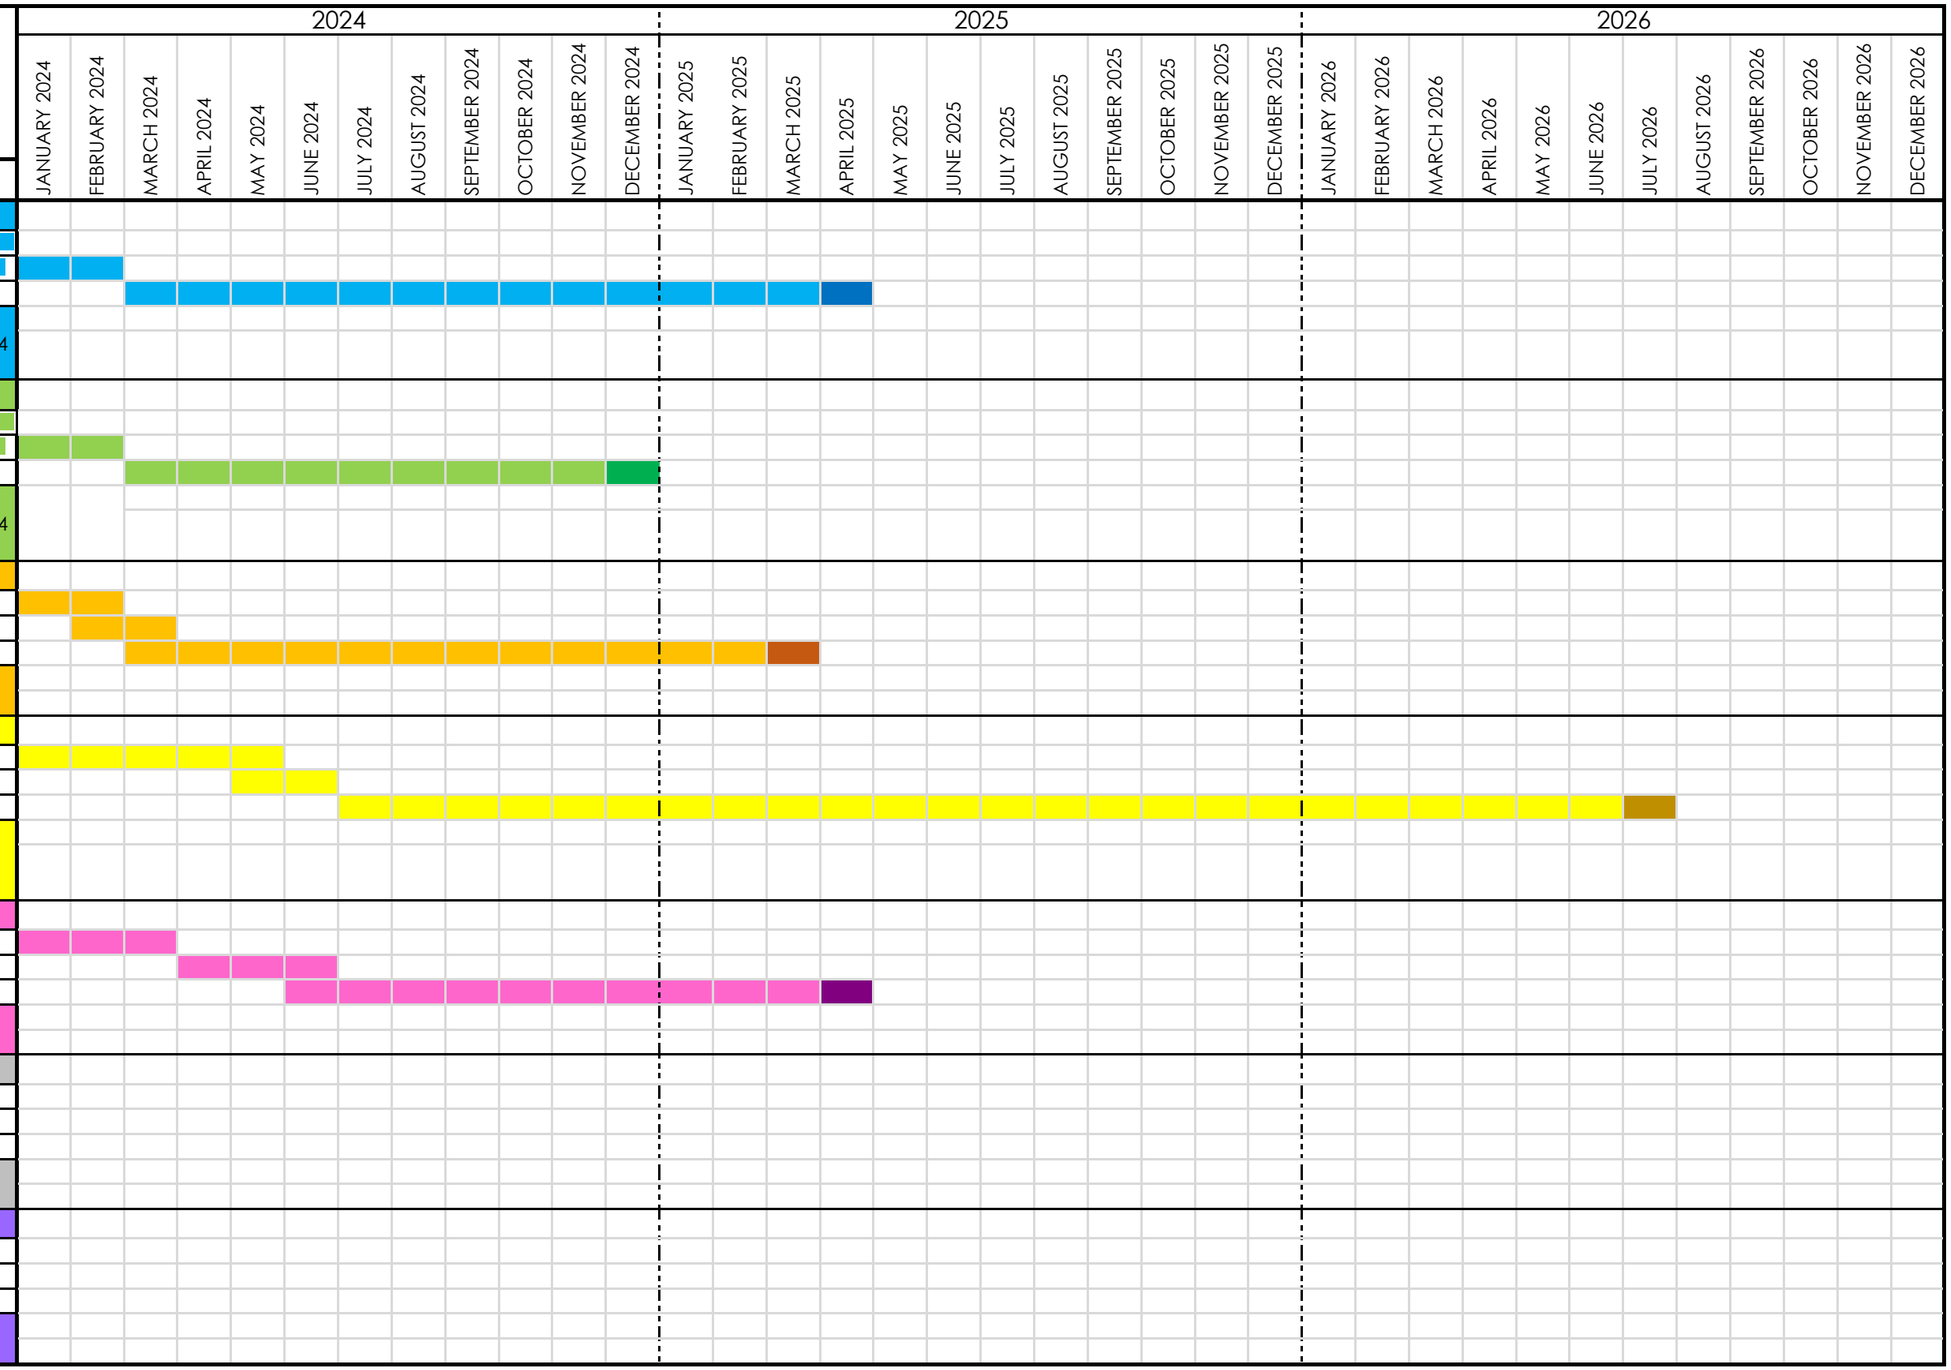
PROJECT	PROGRESS
C & E WING RENOVATION	**68%**
Design	100%
Bidding/ Contract Award	95%
Contruction	10%
NOTES: We are currently waiting on contract award from CDB. I am hopeful that construction will begin in March 2024	
ELEVATOR IN THE WEST LOBBY	**65%**
Design	100%
Bidding/ Contract Award	95%
Contruction	0%
NOTES: We are currently waiting on contract award from CDB. I am hopeful that construction will begin in March 2024	
BASEBALL/SOFT. PLAYER DEV.	**28%**
Design	85%
Bidding/ Contract Award	0%
Contruction	0%
NOTES: Design work is being finalized and will likely begin bidding in February.	
CTE/EDA CONSTRUCTION	**22%**
Design	65%
Bidding/ Contract Award	0%
Contruction	0%
NOTES: BDHG has been working with faculty and staff to ensure that all needs are being met. Full meeting with JALC soon.	
WEST LOBBY EXPANSION	**28%**
Design	85%
Bidding/ Contract Award	0%
Contruction	0%
NOTES: BHDG will be submitting the 100% design documents on 3.15.24. Bidding should happen in May.	
	0%
Design	0%
Bidding/ Contract Award	0%
Contruction	0%
	0%
Design	0%
Bidding/ Contract Award	0%
Contruction	0%
